


ID	Activity	Days	Start	Finish	2018												2019												2020												2021												2022												2023												2024												2025																																																																																																																																																																																													
					J			F			A			M			J			J			A			S			O			N			D			J			F			M			A			M			J			J			A			S			O			N			D			J			F			M			A			M			J			J			A			S			O			N			D																																																																																																																																																																											
					1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26
Kai Tak West Initial Works Programme																																																																																																																																																																																																																																																																																						
All Landside and Marine Side Geotechnical Investigation (KD4A)																																																																																																																																																																																																																																																																																						
S005	Method Statement & Approval	32	05/01/18	10/02/18																																																																																																																																																																																																																																																																																		
S100	Kai Tak Side Geotechnical Investigation & Report	93	12/02/18	09/06/18																																																																																																																																																																																																																																																																																		
S103	Notice to Mariner, Sediment Proposal, Preparation Works, etc	45	05/01/18	01/03/18																																																																																																																																																																																																																																																																																		
S105	Marine Geotechnical Investigation & Report	90	02/03/18	22/06/18																																																																																																																																																																																																																																																																																		
S108	TTM Preparation & Approval and Preparation Works	62	05/01/18	21/03/18																																																																																																																																																																																																																																																																																		
S110	Ma Tau Kok Side Geotechnical Investigation & Report	81	22/03/18	03/07/18																																																																																																																																																																																																																																																																																		
S120	KD 4A	0		03/07/18*																																																																																																																																																																																																																																																																																		
Demolition of Landside Structures of KCFP and Carpark Re-provisioning (KD01)																																																																																																																																																																																																																																																																																						
S123	Possess Portion 1B	0		03/04/18*																																																																																																																																																																																																																																																																																		
S125	Preparation & Approval of Ramp & Carpark Buildings	24	05/01/18	01/02/18																																																																																																																																																																																																																																																																																		
S126	Portion 1B Building Survey Report & Approval	40	02/02/18	23/03/18																																																																																																																																																																																																																																																																																		
S127	Preparation & Approval of TTA Schemes	96	05/01/18	05/05/18																																																																																																																																																																																																																																																																																		
S128	Preparation & Approval of Temp Work Design	66	05/01/18	26/03/18																																																																																																																																																																																																																																																																																		
S129	Asbestos Inspection and Submit Report to EPD	96	31/01/18*	01/06/18																																																																																																																																																																																																																																																																																		
S130	Site Hoarding and Remove Existing Furniture	26	05/04/18	05/05/18																																																																																																																																																																																																																																																																																		
S132	Public Interchange Modification Works (TTM Stage 1-4)	58	07/05/18	16/07/18																																																																																																																																																																																																																																																																																		
S135	Protection Work and Demolish Carpark Building	30	02/06/18	09/07/18																																																																																																																																																																																																																																																																																		
S136	Protection Work and Demolish Carpark Ramp Structure	60	07/05/18	18/07/18																																																																																																																																																																																																																																																																																		
S150	Roadwork to Provide New Parking Facilities in Portion 1B	40	19/07/18	03/09/18																																																																																																																																																																																																																																																																																		
S155	Implement TTM Stage 5	1	04/09/18	04/09/18																																																																																																																																																																																																																																																																																		
S160	KD 01	0		04/09/18*																																																																																																																																																																																																																																																																																		
Trees Felling and Protection in Portion 1B (San Ma Tau St) (KD12)																																																																																																																																																																																																																																																																																						
S165	Trees Proposal & Preparation Works	90	05/01/18	27/04/18																																																																																																																																																																																																																																																																																		
S170	Tree Felling, T483-T485, T532-T533	24	28/04/18	28/05/18																																																																																																																																																																																																																																																																																		
S180	Tree Protection, T486	12	29/05/18	11/06/18																																																																																																																																																																																																																																																																																		
S190	KD 12	0		04/09/18*																																																																																																																																																																																																																																																																																		
Vertical Wall in Portion 3B CH 4759-CH 5085 (KD7A)																																																																																																																																																																																																																																																																																						
S195	Submission & Approval and Preparation Works	85	05/01/18	21/04/18																																																																																																																																																																																																																																																																																		
S200	Pipe Piles along North Wall	186	23/04/18	03/12/18																																																																																																																																																																																																																																																																																		
S222	Type IV Sheetpile	68	16/10/18	07/01/19																																																																																																																																																																																																																																																																																		
S225	Demobilisation	12	08/01/19	21/01/19																																																																																																																																																																																																																																																																																		
S226	Fencing and Site Clearance for Handover Area	30	22/01/19	28/02/19																																																																																																																																																																																																																																																																																		
S230	KD 7A (Handover Portion 3B)	0		31/12/18*																																																																																																																																																																																																																																																																																		
Dumping Permit, Barging Point, Structural Assessment of Marine Side KCFP (KD4B)																																																																																																																																																																																																																																																																																						
S235	Submission and Approval of Sampling Plan	32	05/01/18	10/02/18																																																																																																																																																																																																																																																																																		
S240	Field Sampling and Testing	164	12/02/18	03/09/18																																																																																																																																																																																																																																																																																		
S250	Preparation and Approval for Sediment Quality Report	50	04/09/18	03/11/18																																																																																																																																																																																																																																																																																		
S260	Application for Dumping Permit	50	05/11/18	04/01/19																																																																																																																																																																																																																																																																																		
S265	Submission & Approval and Preparation Works	46	05/01/18	02/03/18																																																																																																																																																																																																																																																																																		
S270	Carry Out Structural assessment of KCFP (Marine Portion)	250	03/03/18	04/01/19																																																																																																																																																																																																																																																																																		
S275	Design & Procurement	120	05/01/18	04/06/18																																																																																																																																																																																																																																																																																		
S280	Construct Barging Point	204	02/05/18	04/01/19																																																																																																																																																																																																																																																																																		
S290	KD 4B	0		04/01/19*																																																																																																																																																																																																																																																																																		
Ventilation Adit at Eastern Interface CH 5020-5082 (KD4C)																																																																																																																																																																																																																																																																																						
S295	Submission & Approval and Preparation Works	90	05/01/18	27/04/18																																																																																																																																																																																																																																																																																		
S300	Piling & Pumping Test	159	28/04/18	07/11/18																																																																																																																																																																																																																																																																																		




CONTRACT NO. HY2014/07
CENTRAL KOWLOON ROUTE - KAI TAK WEST
INITIAL WORKS PROGRAMME (IWP)

Page 1	Date	Revision	Checked	Approved
	05 Jan 18	IWP		

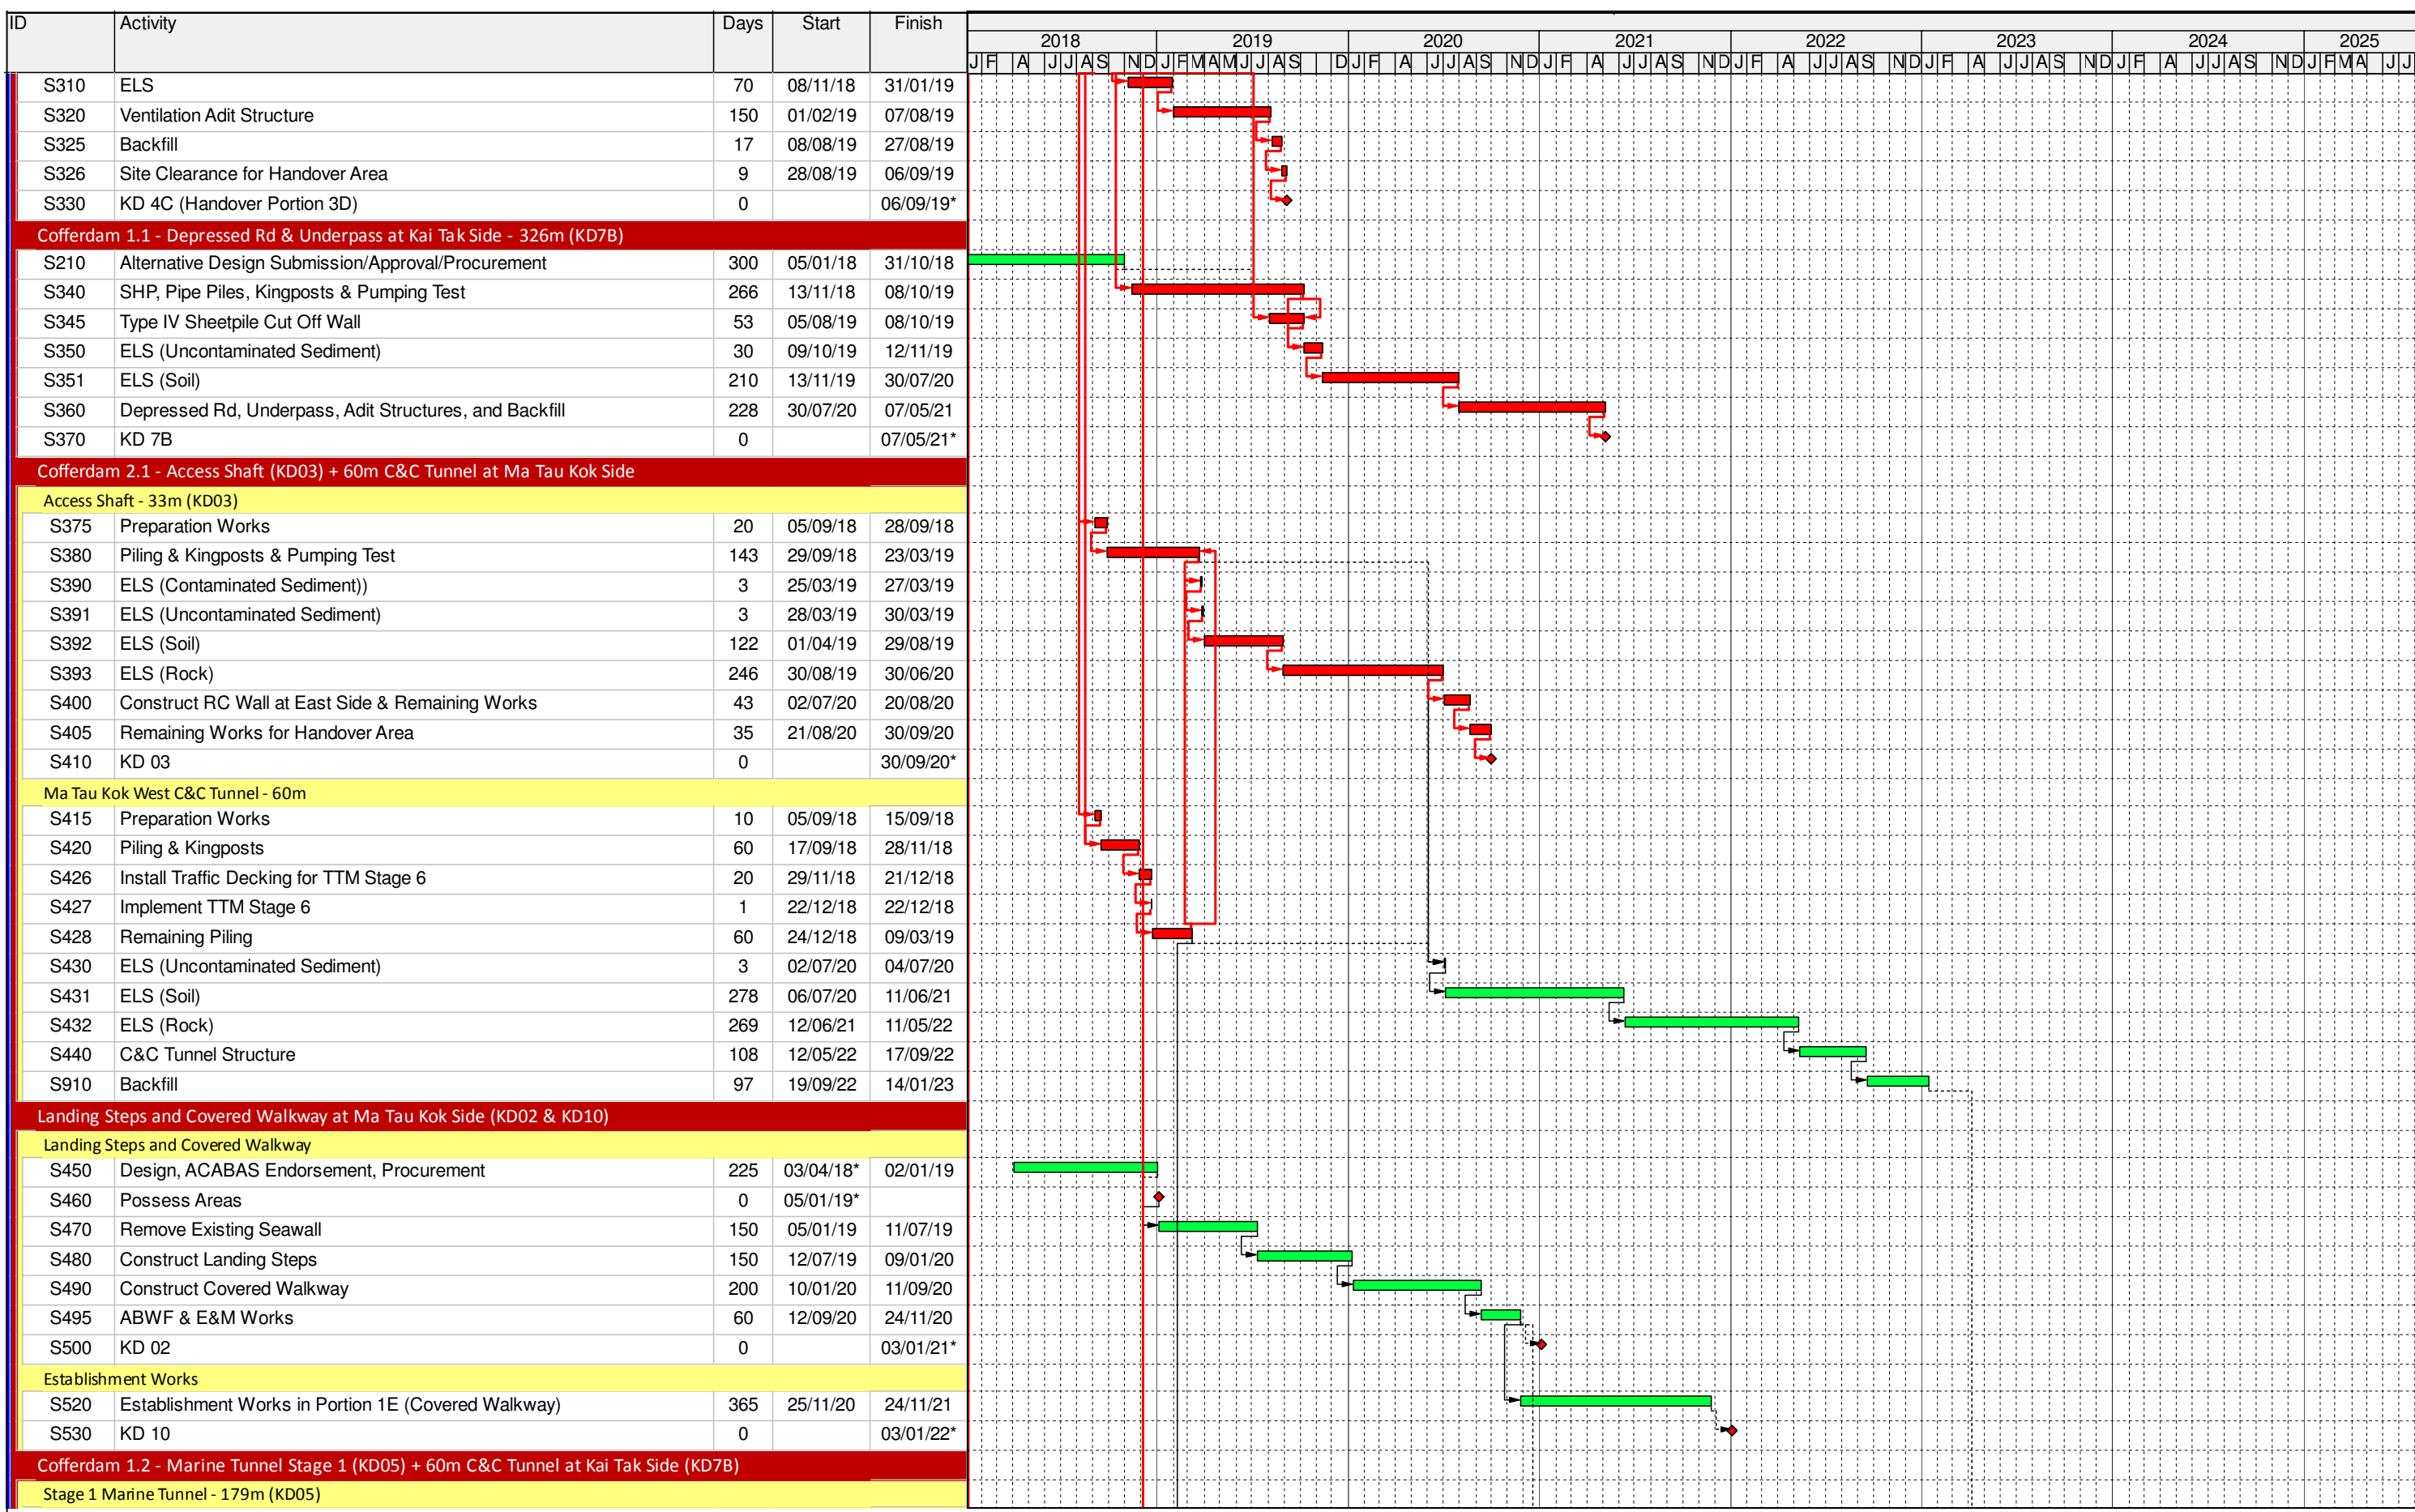

CONTRACT NO. HY2014/07
 CENTRAL KOWLOON ROUTE - KAI TAK WEST
 INITIAL WORKS PROGRAMME (IWP)

Date	Revision	Checked	Approved
05 Jan 18	IWP		

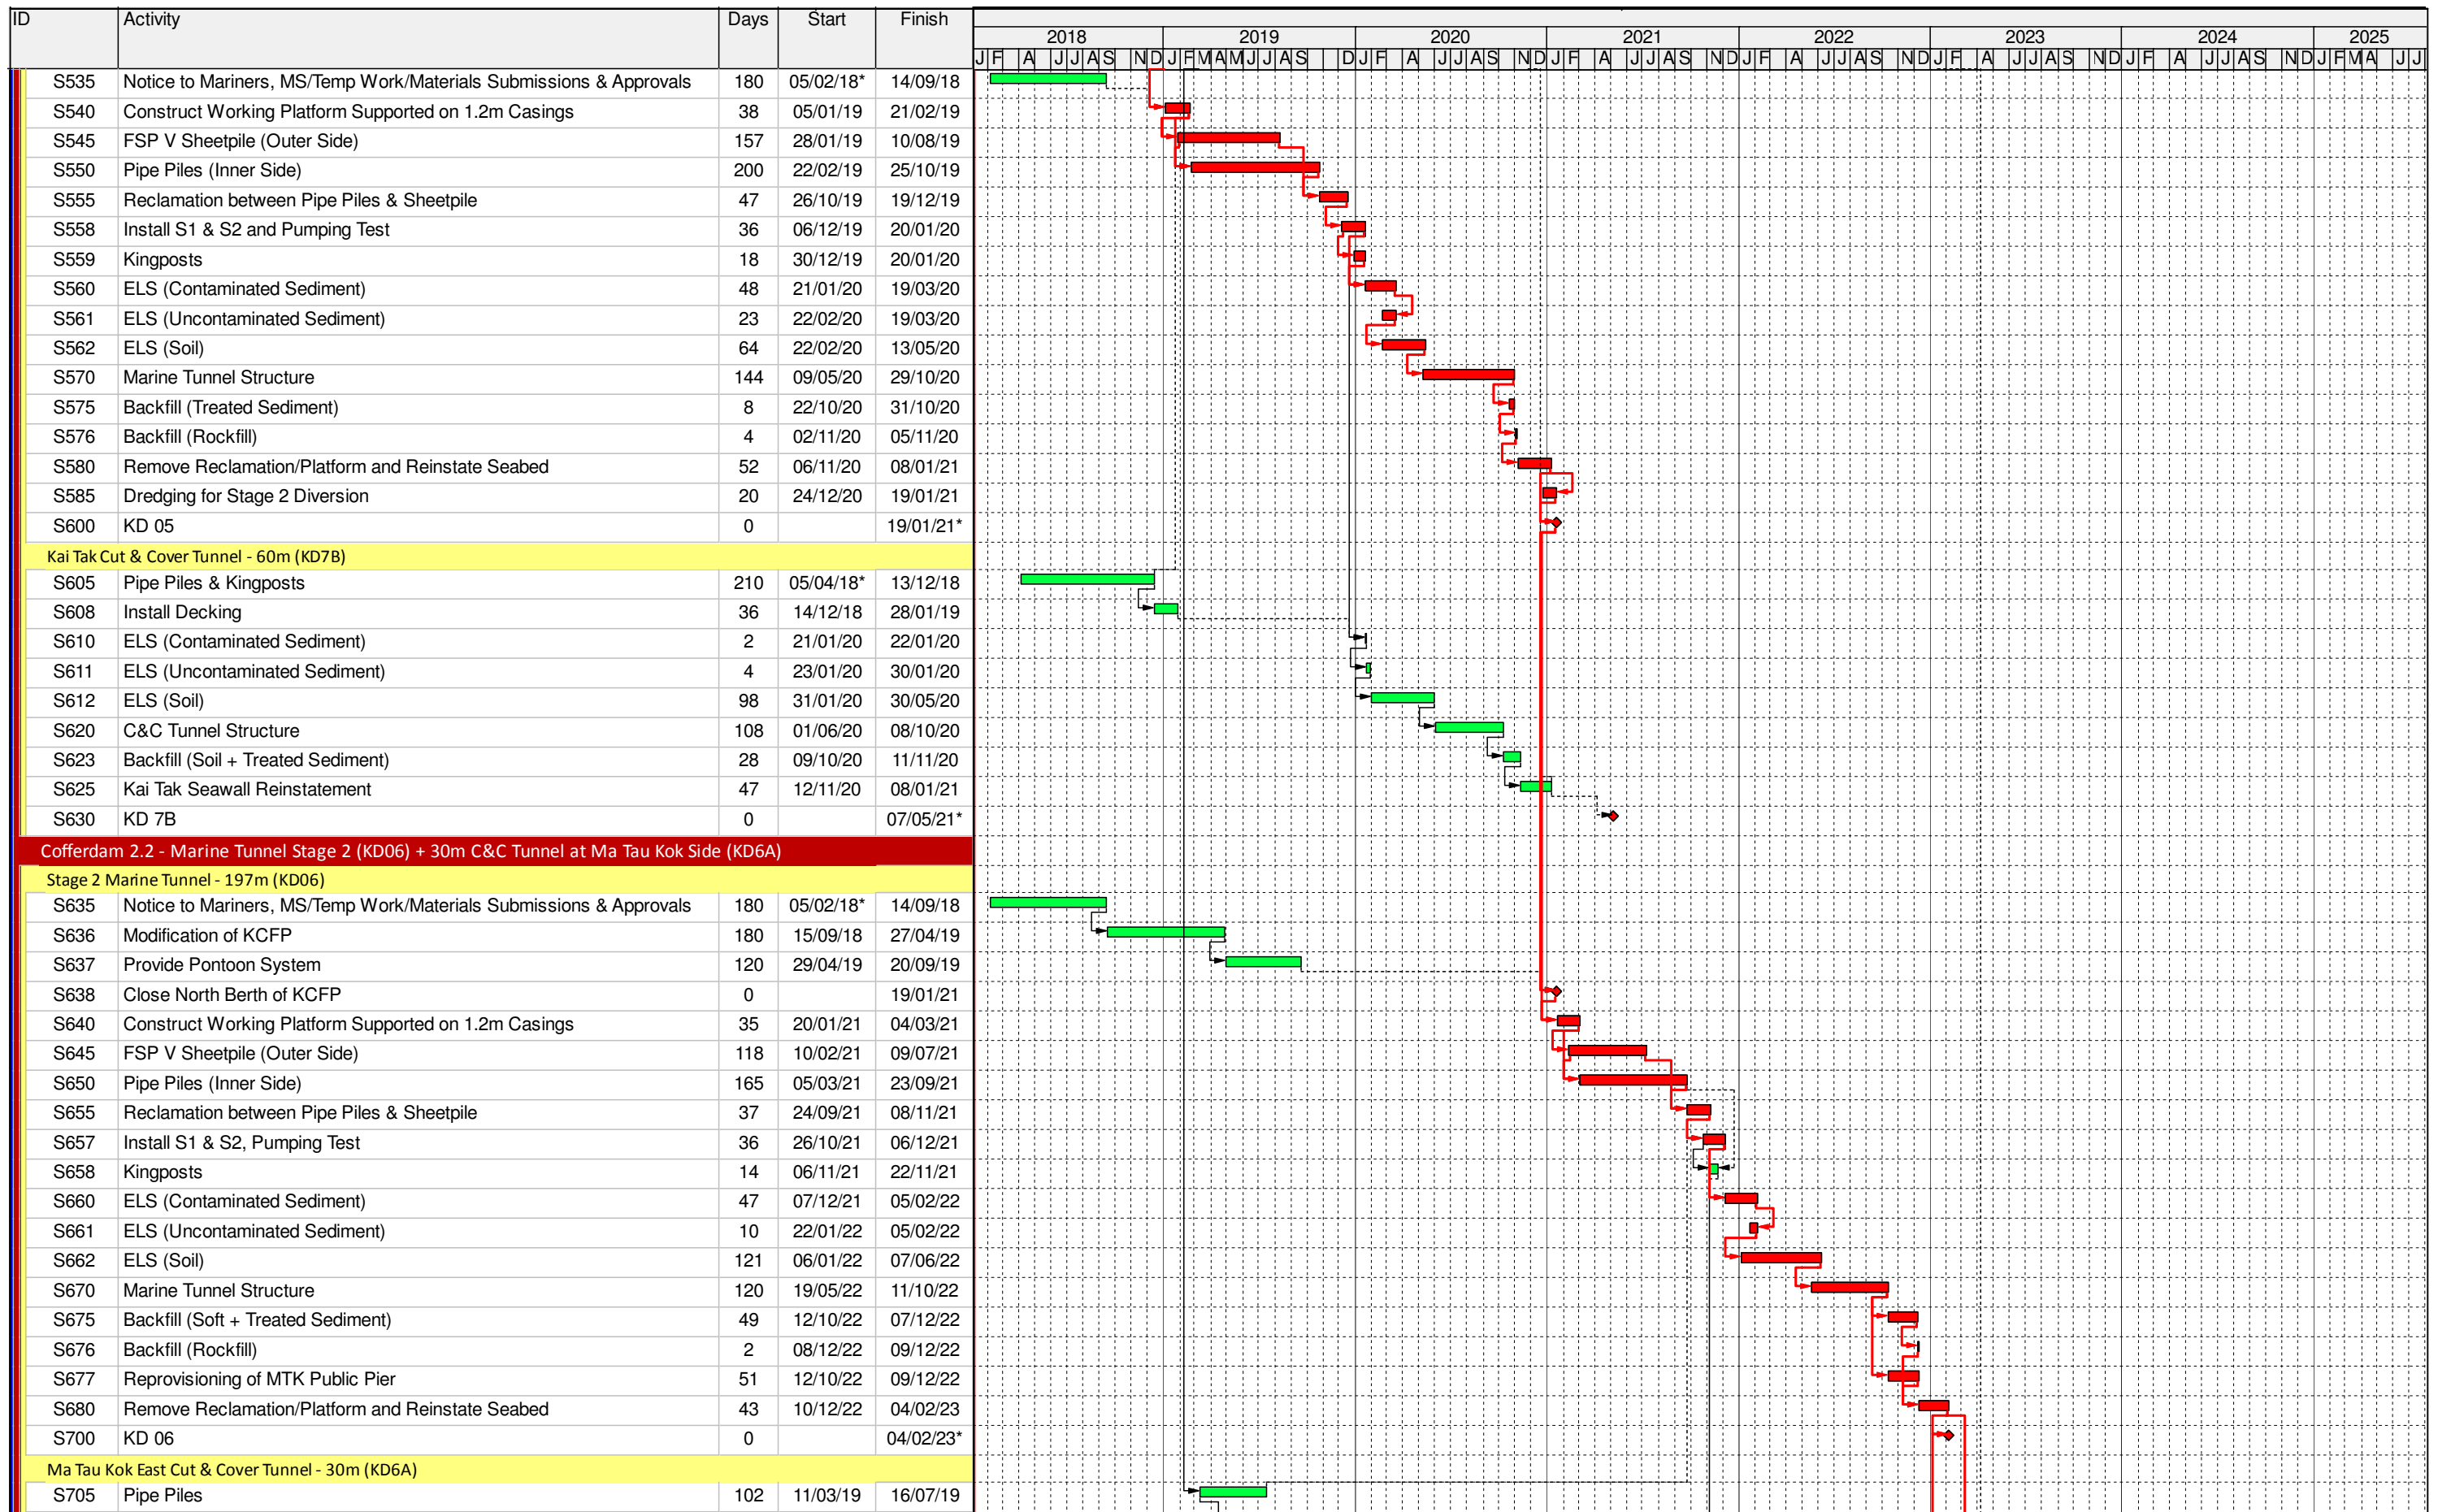

CONTRACT NO. HY2014/07
 CENTRAL KOWLOON ROUTE - KAI TAK WEST
 INITIAL WORKS PROGRAMME (IWP)

Date	Revision	Checked	Approved
05 Jan 18	IWP		

