


Appendix F - 24-hour TSP Monitoring Results

Location M-A3 - S.K.H. Tsoi Kung Po Secondary School

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (hrs.)	Flow Rate (m³/min.)		Av. Flow (m³/min)	Total vol. (m³)	Conc. (µg/m³)	Action Level (µg/m3)	Limit Level (µg/m4)
				Initial	Final		Initial	Final		Initial	Final					
1-Apr-25	Sunny	290.4	765.0	2.8211	2.8871	0.0660	13195.5	13219.5	24.0	1.22	1.21	1.21	1749.0	37.7	153.0	<u>260.0</u>
5-Apr-25	Sunny	292.9	762.7	3.3484	3.4386	0.0901	13219.5	13243.5	24.0	1.21	1.21	1.21	1737.6	51.9		
11-Apr-25	Sunny	297.8	757.8	3.3917	3.4419	0.0502	13243.5	13267.5	24.0	1.21	1.21	1.21	1742.0	28.8		
16-Apr-25	Fine	297.3	759.4	3.3862	3.5386	0.1523	13267.5	13291.5	24.0	1.21	1.21	1.21	1745.9	87.3		
22-Apr-25	Sunny	300.6	758.4	2.7554	2.8260	0.0706	13291.5	13315.5	24.0	1.20	1.20	1.20	1733.7	40.7		
26-Apr-25	Fine	295.3	761.5	2.8202	2.8877	0.0675	13315.5	13339.5	24.0	1.22	1.22	1.22	1755.4	38.5		
													Min	28.8		
													Max	87.3		
													Average	47.5		

24-hr TSP Concentration Levels

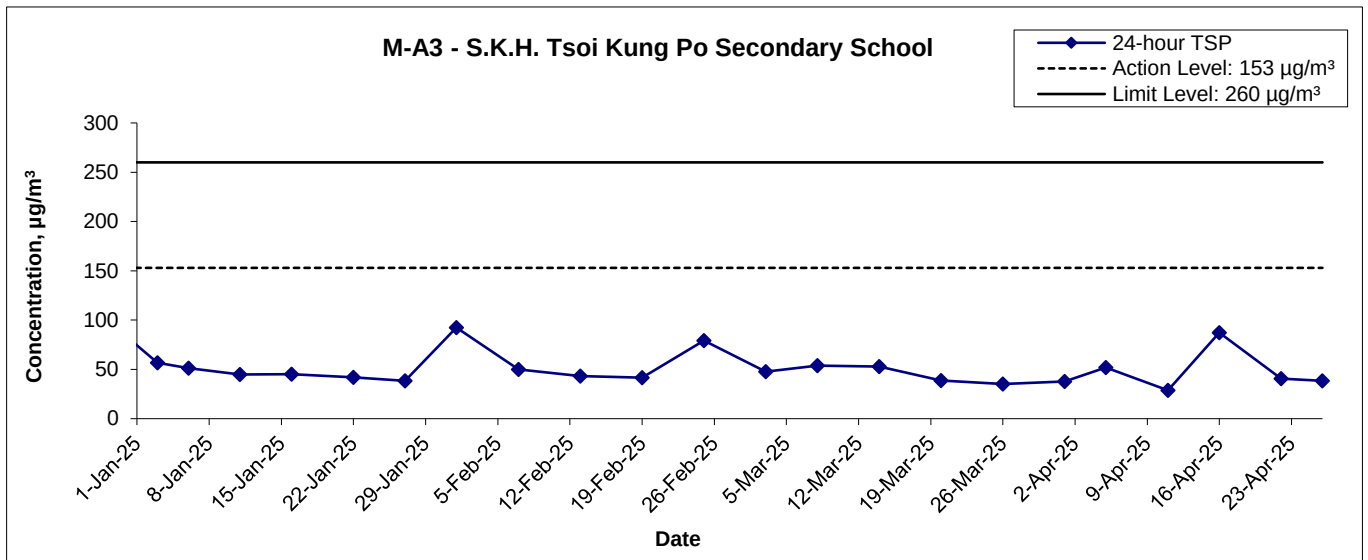

Title	Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Graphical Presentation of 24-hour TSP Monitoring Results	Scale	Project	CINOTECH
		N.T.S Date Apr 25	No. MA20024 Appendix F	
