

Appendix H Regular Construction Noise Monitoring Results

Daytime Noise Monitoring Results at Station E-N12a (19 Hing Yan Street)

Date	Weather Condition	Noise Level for 30-min, dB(A) ⁺				Limit Level, dB(A)	Exceedance (Y/N)
		Time	L90	L10	Leq		
3-Aug-21	Fine	11:20	60.9	65.2	63.7	75	N
9-Aug-21	Fine	11:05	64.6	68.1	67.4	75	N
20-Aug-21	Sunny	13:38	62.9	67.4	65.7	75	N
26-Aug-21	Sunny	11:20	64.9	68.9	67.2	75	N



Daytime Noise Monitoring Results at Station E-N21a (Block B of Merit Industrial Centre)

Date	Weather Condition	Noise Level for 30-min, dB(A) [#]				Limit Level, dB(A)	Exceedance (Y/N)
		Time	L90	L10	Leq		
3-Aug-21	Fine	15:15	62.0	66.5	65.2	75	N
9-Aug-21	Fine	16:00	65.3	69.6	67.9	75	N
20-Aug-21	Sunny	13:00	61.4	63.8	62.1	75	N
26-Aug-21	Sunny	15:25	62.5	67.0	64.9	75	N

⁺ - Façade measurement.

[#] - A correction of +3dB(A) was made to the free field measurement.

^{*} - Limit Level of 70dB(A) applies to education institutes while 65dB(A) applies during school examination

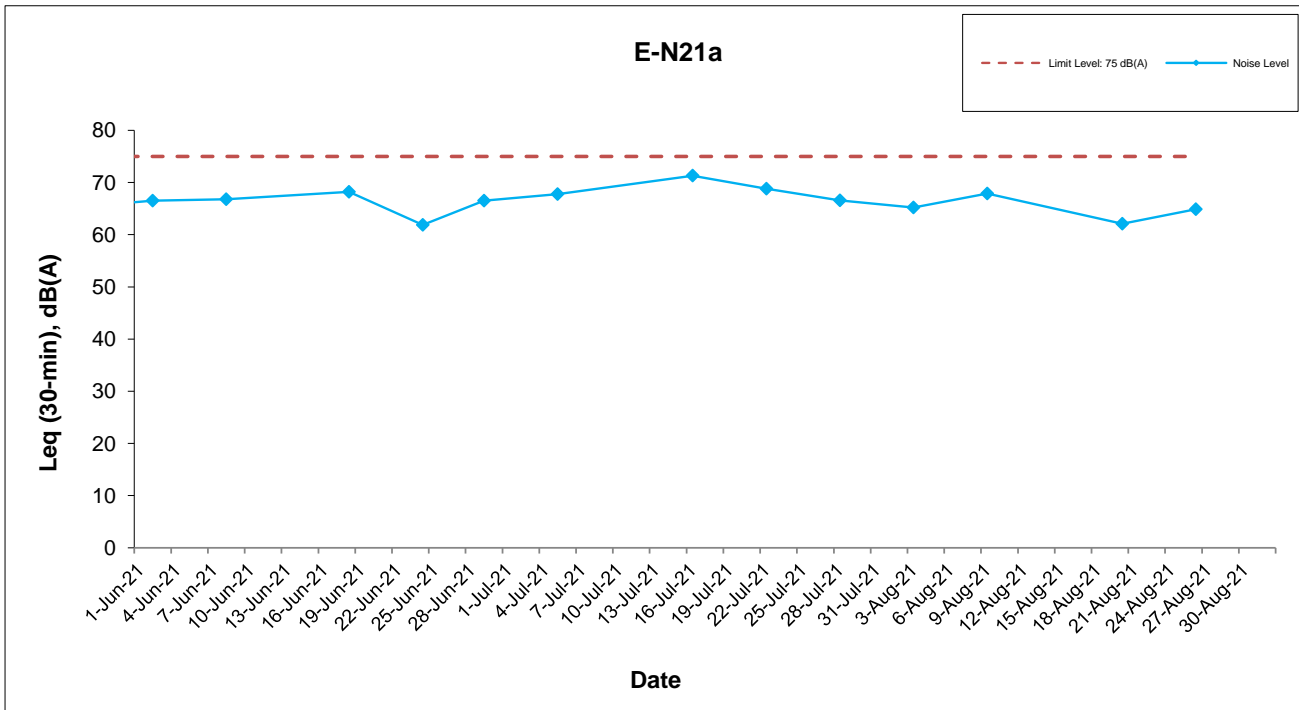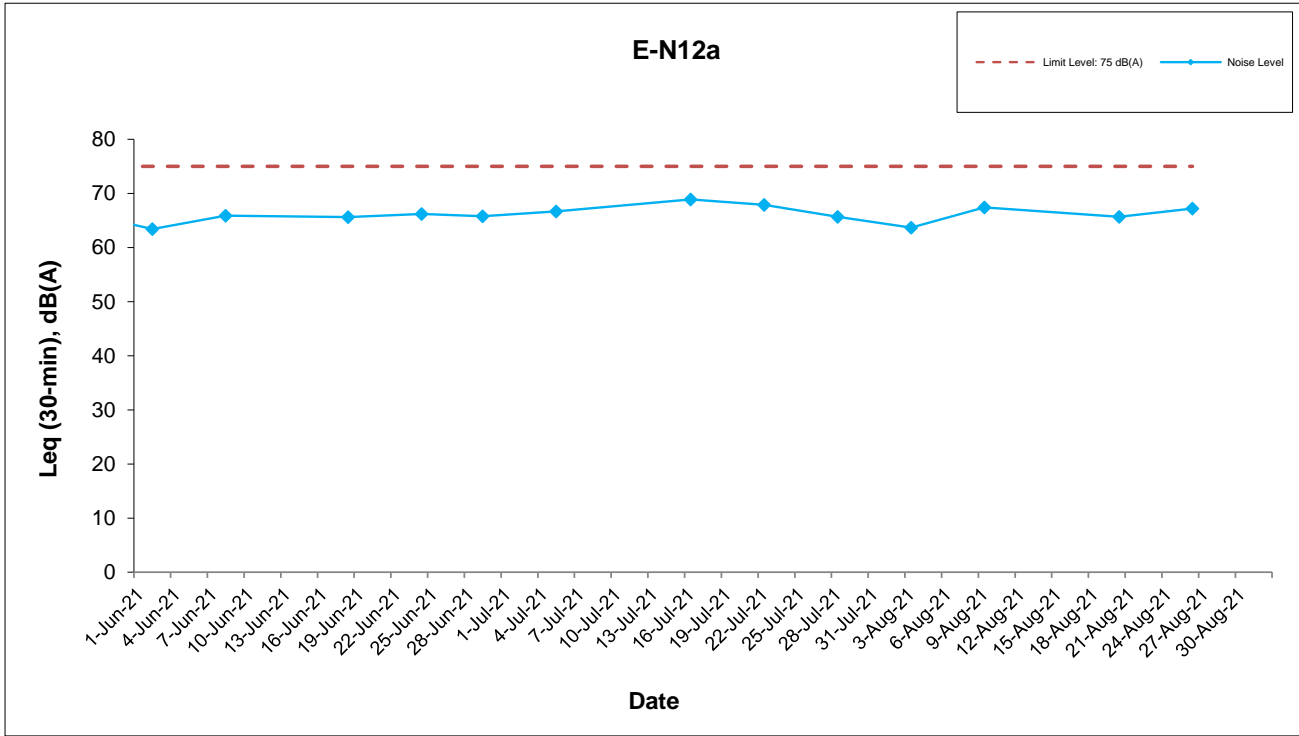

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Central Kowloon Route - Kai Tak West (Contract No. HY/2014/07)



Graphical Presentation of Impact Noise Monitoring Results

Date: September 2021

Appendix H
