


Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Limit Level - 70.0 dB(A) / School Exam - 65.0 dB(A)

Location M-N3 - S.K.H. Tsoi Kung Po Secondary School							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
05-Aug-24	11:15	Sunny	67.1	68.9	56.5	67.7	67.1 Measured \leq Baseline
15-Aug-24	10:00	Cloudy	69.1	71.5	63.2	67.7	63.5
21-Aug-24	16:32	Cloudy	67.6	70.9	60.1	67.7	67.6 Measured \leq Baseline
27-Aug-24	16:00	Sunny	64.9	67.3	61.4	67.7	64.9 Measured \leq Baseline

Noise Levels

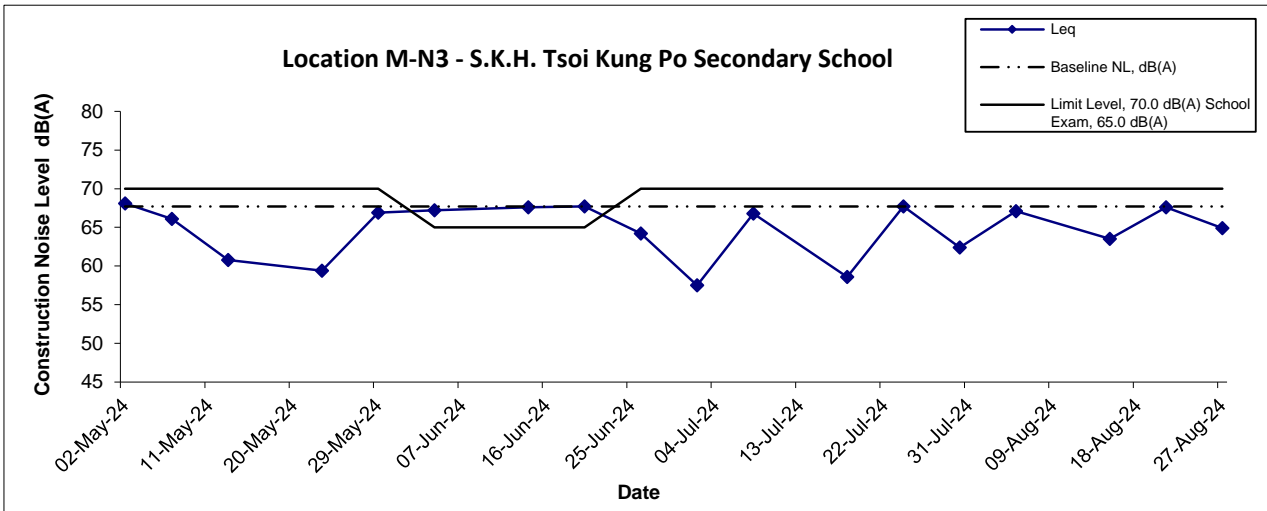

Title Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA20024	
	Date Aug-24	Appendix G	
