

Appendix H Regular Construction Noise Monitoring Results

Daytime Noise Monitoring Results at Station E-N12a (19 Hing Yan Street)



Date	Weather Condition	Noise Level for 30-min, dB(A) ⁺				Limit Level, dB(A)	Exceedance (Y/N)
		Time	L90	L10	Leq		
2-Dec-21	Fine	14:30	66.8	72.0	70.4	75	N
8-Dec-21	Fine	13:34	62.9	70.3	67.1	75	N
14-Dec-21	Fine	13:05	66.5	70.1	68.7	75	N
20-Dec-21	Cloudy	13:40	69.0	71.7	70.1	75	N
29-Dec-21	Sunny	11:10	69.6	72.6	70.9	75	N

Daytime Noise Monitoring Results at Station E-N21a (Block B of Merit Industrial Centre)

Date	Weather Condition	Noise Level for 30-min, dB(A) [#]				Limit Level, dB(A)	Exceedance (Y/N)
		Time	L90	L10	Leq		
2-Dec-21	Fine	13:15	63.4	67.8	65.3	75	N
8-Dec-21	Fine	14:25	60.8	64.4	63.1	75	N
14-Dec-21	Fine	14:00	64.1	67.0	66.2	75	N
20-Dec-21	Cloudy	13:00	63.5	66.6	65.2	75	N
29-Dec-21	Sunny	10:15	61.4	65.6	64.8	75	N

⁺ - Façade measurement.

[#] - A correction of +3dB(A) was made to the free field measurement.

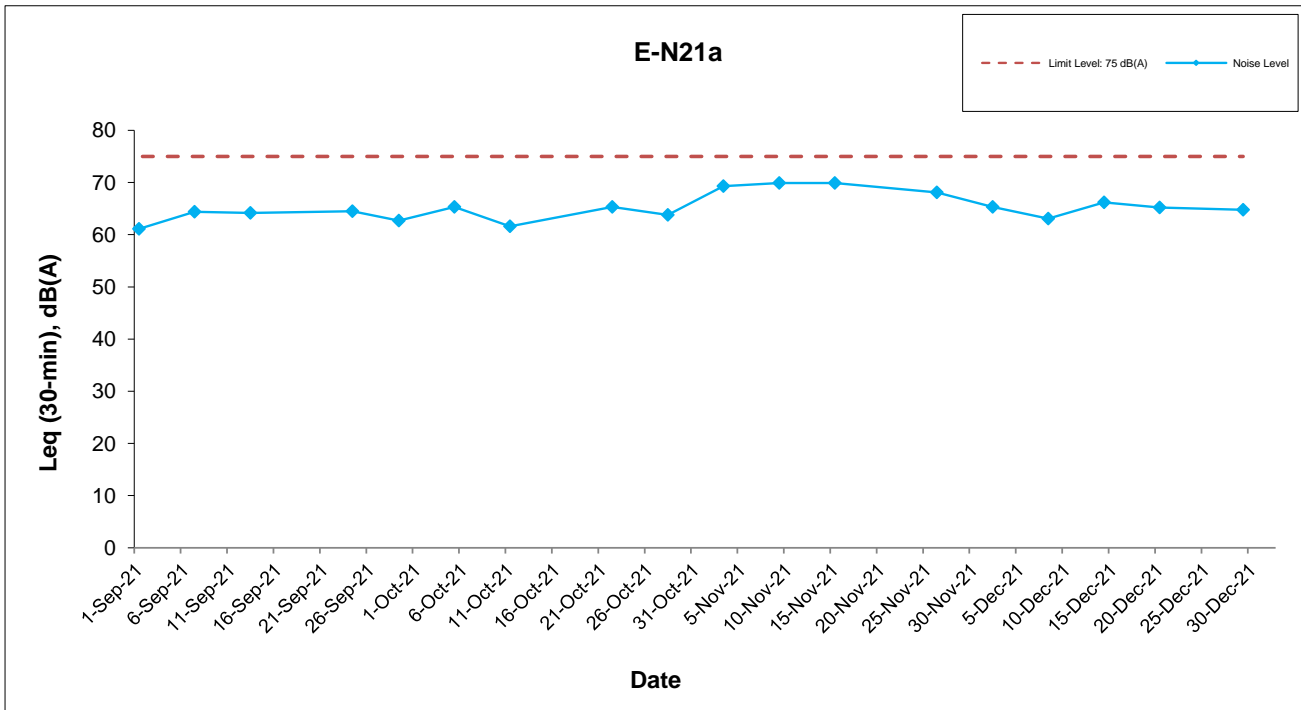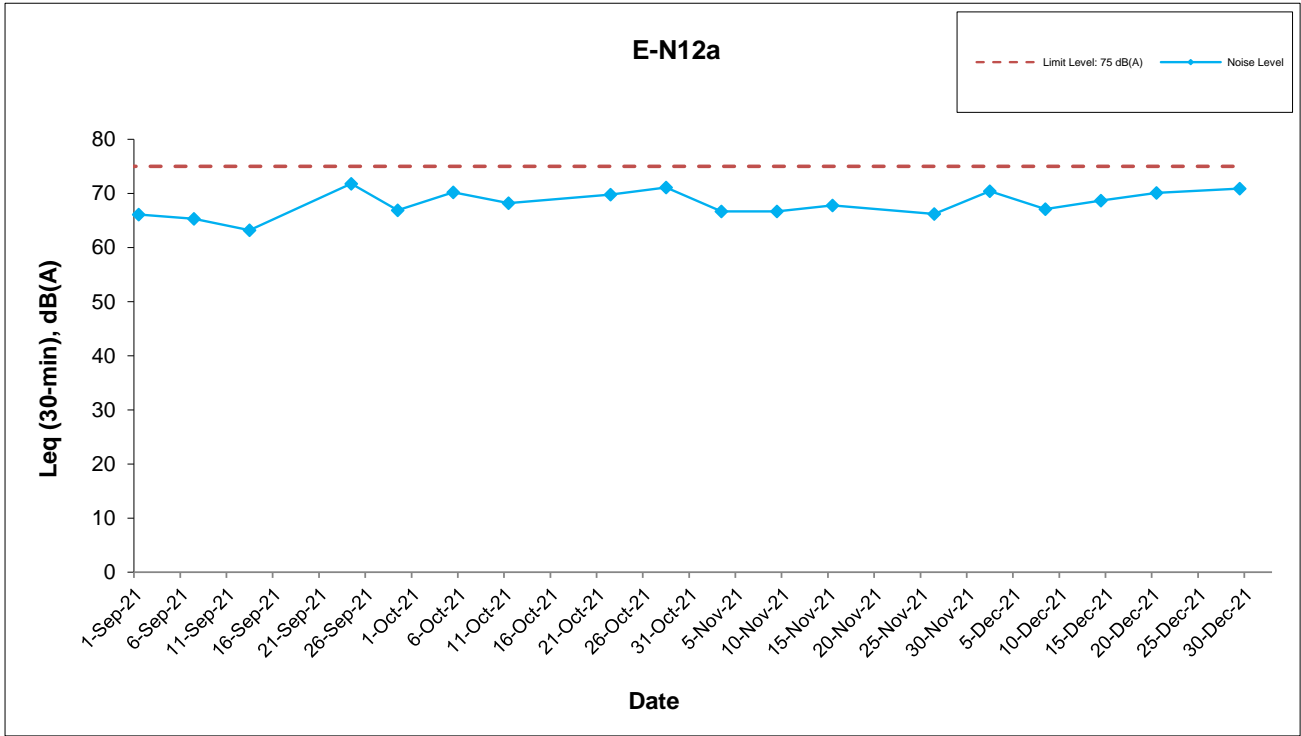

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Central Kowloon Route - Kai Tak West (Contract No. HY/2014/07)



Graphical Presentation of Impact Noise Monitoring Results

Date: January 2022

Appendix H
