


Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)
Limit Level - 70.0 dB(A) / School Exam - 65.0 dB(A)

Location M-N3 - S.K.H. Tsoi Kung Po Secondary School							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
01-Dec-25	14:30	Fine	65.9	68.3	60.1	67.7	65.9 Measured ≤ Baseline
11-Dec-25	16:28	Fine	68.9	71.2	61.2	67.7	62.7
17-Dec-25	14:17	Sunny	65.6	67.9	55.6	67.7	65.6 Measured ≤ Baseline
23-Dec-25	15:25	Cloudy	65.9	67.7	56.6	67.7	65.9 Measured ≤ Baseline
29-Dec-25	16:41	Fine	65.7	68.2	57.6	67.7	66 Measured ≤ Baseline

Noise Levels

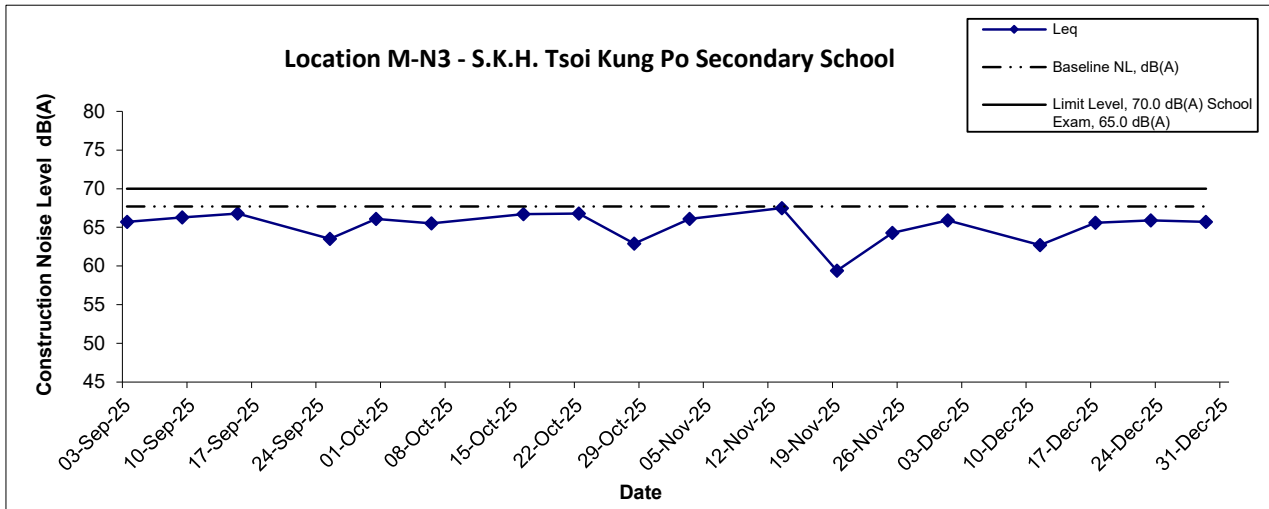

Title Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA20024	CINOTECH
	Date Dec-25	Appendix G	
