


## Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Limit Level - 70.0 dB(A) / School Exam - 65.0 dB(A)

Location M-N3 - S.K.H. Tsoi Kung Po Secondary School							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
07-Jan-25	16:40	Fine	66.6	69.3	55.8	67.7	66.6 Measured $\leq$ Baseline
13-Jan-25	16:00	Fine	66.4	68.3	57.2	67.7	66.4 Measured $\leq$ Baseline
23-Jan-25	13:30	Fine	66.8	69.0	58.8	67.7	66.8 Measured $\leq$ Baseline
28-Jan-25	11:00	Fine	64.0	68.2	55.9	67.7	64 Measured $\leq$ Baseline

## Noise Levels

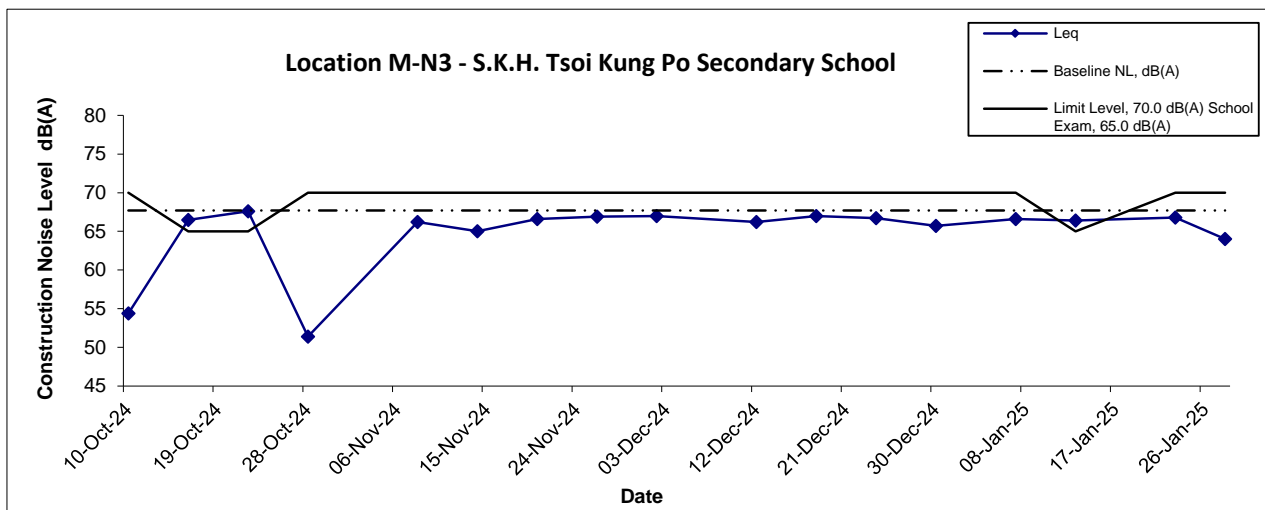

Title Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works  Graphical Presentation of Construction Noise Monitoring Results	Scale	N.T.S	Project	No. MA20024	CINOTECH
	Date	Jan-25	Appendix	G	
