Appendix H Regular Construction Noise Monitoring Results

Daytime Noise Monitoring Results at Station E-N12a (19 Hing Yan Street)

Date	Weather Condition	Noise Level for 30-min, dB(A) ⁺				Limit Level,	Exceedance
		Time	L90	L10	Leq	dB(A)	(Y/N)
2-Jul-20	Cloudy	10:50	64.3	68.1	66.5	75	N
8-Jul-20	Fine	11:15	64.7	68.0	66.5	75	N
14-Jul-20	Sunny	11:25	64.0	68.5	67.6	75	N
20-Jul-20	Sunny	15:00	64.7	67.6	66.3	75	N
31-Jul-20	Cloudy	10:40	66.2	68.0	67.1	75	N


Daytime Noise Monitoring Results at Station E-N21a (Block B of Merit Industrial Centre)


Date	Weather Condition	Noise Level for 30-min, dB(A) #				Limit Level,	Exceedance
		Time	L90	L10	Leq	dB(A)	(Y/N)
2-Jul-20	Cloudy	10:05	67.2	68.9	68.0	75	N
8-Jul-20	Fine	10:20	63.9	68.5	66.8	75	N
14-Jul-20	Sunny	13:45	58.5	60.5	60.1	75	N
20-Jul-20	Sunny	14:10	63.8	67.2	66.0	75	N
31-Jul-20	Cloudy	9:20	67.1	68.9	68.0	75	N

⁺ - Façade measurement.

^{# -} A correction of +3dB(A) was made to the free field measurement.

^{* -} Limit Level of 70dB(A) applies to education institutes while 65dB(A) applies during school

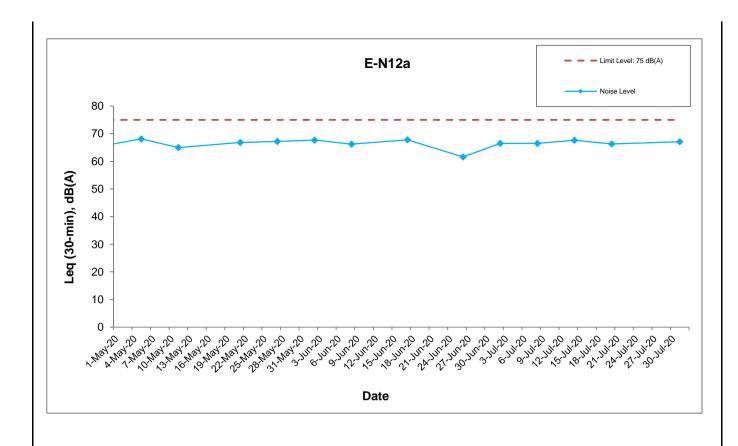

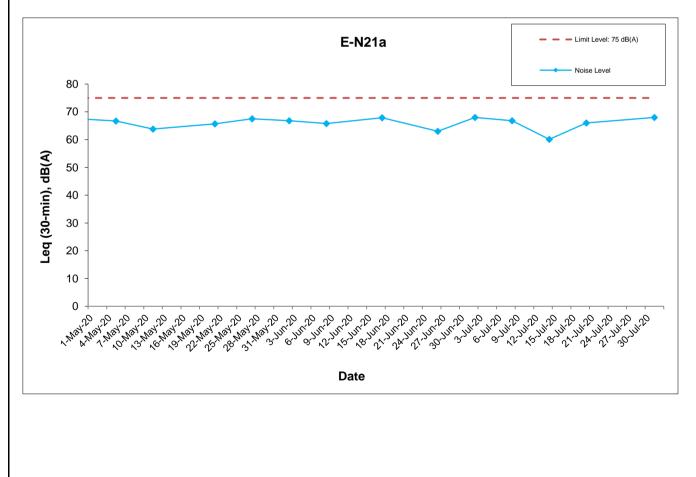

This Drawing has been prepared for the use of AECON's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECON or as required by Central Kowloon Route - Kai Tak West (Contract No. HY/2014/07)

Date: August 2020

