


Appendix F - 24-hour TSP Monitoring Results

Location M-A3 - S.K.H. Tsoi Kung Po Secondary School

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (hrs.)	Flow Rate (m ³ /min.)		Av. Flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)	Action Level (µg/m ³)	Limit Level (µg/m ⁴)
				Initial	Final		Initial	Final		Initial	Final					
3-Jun-24	Rainy	297.7	757.9	3.3305	3.3835	0.0530	11851.4	11875.4	24.0	1.22	1.22	1.22	1756.8	30.2	153.0	<u>260.0</u>
7-Jun-24	Cloudy	299.0	756.5	3.3987	3.4395	0.0408	11875.4	11899.4	24.0	1.22	1.21	1.22	1750.9	23.3		
13-Jun-24	Rainy	302.8	754.3	3.3787	3.4112	0.0325	11899.4	11923.4	24.0	1.21	1.21	1.21	1743.5	18.6		
19-Jun-24	Cloudy	303.0	755.2	3.3756	3.4129	0.0372	11923.4	11947.4	24.0	1.21	1.21	1.21	1744.1	21.4		
25-Jun-24	Cloudy	303.3	758.7	3.3583	3.4044	0.0461	11947.4	11971.4	24.0	1.21	1.21	1.21	1747.7	26.4		
29-Jun-24	Fine	302.8	756.3	3.3096	3.3458	0.0361	11971.4	11995.4	24.0	1.21	1.21	1.21	1746.3	20.7		
													Min	18.6		
													Max	30.2		
													Average	23.4		

24-hr TSP Concentration Levels

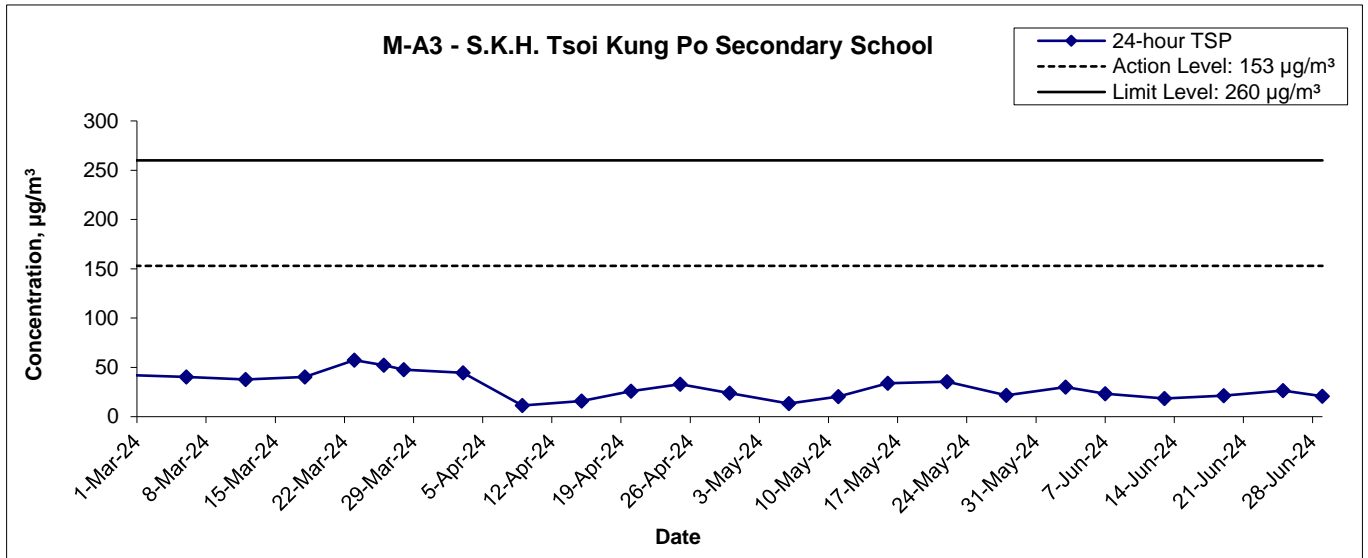

Title Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Graphical Presentation of 24-hour TSP Monitoring Results	Scale N.T.S	Project No. MA20024	
	Date Jun 24	Appendix F	
