


## Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Limit Level - 70.0 dB(A) / School Exam - 65.0 dB(A)

Location M-N3 - S.K.H. Tsoi Kung Po Secondary School							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
04-Jun-24	15:32	Cloudy	67.2	68.9	59.6	67.7	67.2 Measured $\leq$ Baseline
14-Jun-24	14:14	Fine	67.6	70.6	61.2	67.7	67.6 Measured $\leq$ Baseline
20-Jun-24	15:04	Sunny	67.7	70.6	61.4	67.7	67.7 Measured $\leq$ Baseline
26-Jun-24	14:24	Fine	69.3	70.3	61.0	67.7	64.2

## Noise Levels

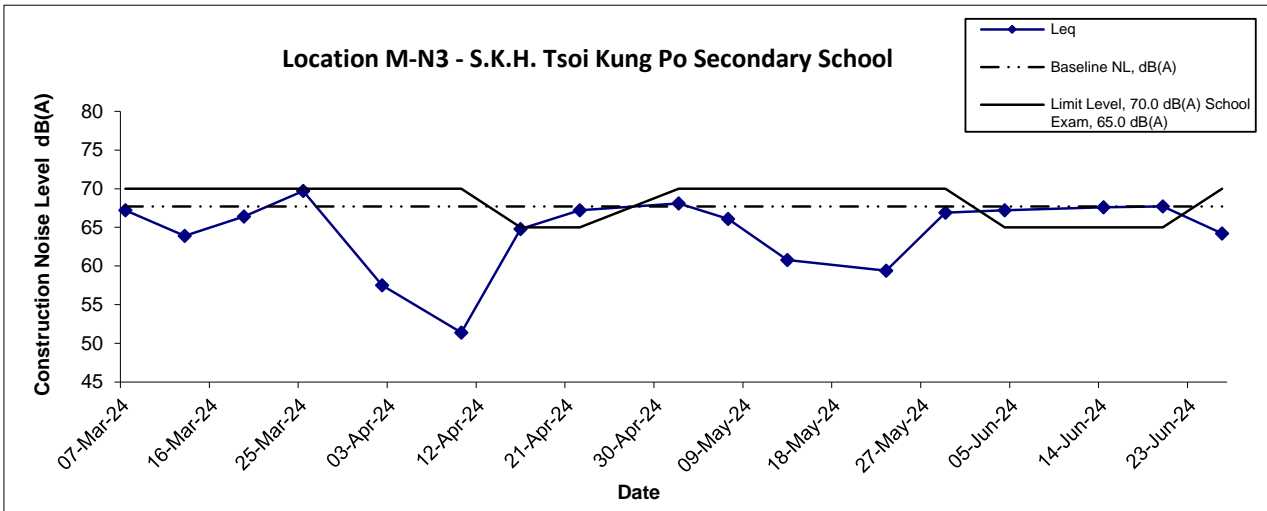

Title Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works  Graphical Presentation of Construction Noise Monitoring Results	Scale	N.T.S	Project	No. MA20024	CINOTECH
	Date	Jun-24	Appendix	G	
