


Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Limit Level - 70.0 dB(A) / School Exam - 65.0 dB(A)

| Location M-N3 - S.K.H. Tsoi Kung Po Secondary School | | | | | | | |
|--|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 07-Mar-24 | 14:59 | Fine | 67.2 | 70.0 | 60.6 | 67.7 | 67.2 Measured ≤ Baseline |
| 13-Mar-24 | 13:56 | Cloudy | 69.2 | 70.7 | 62.2 | 67.7 | 64 |
| 19-Mar-24 | 14:13 | Fine | 66.4 | 68.9 | 60.4 | 67.7 | 66.4 Measured ≤ Baseline |
| 25-Mar-24 | 16:12 | Sunny | 71.8 | 74.3 | 67.0 | 67.7 | 69.7 |

Noise Levels

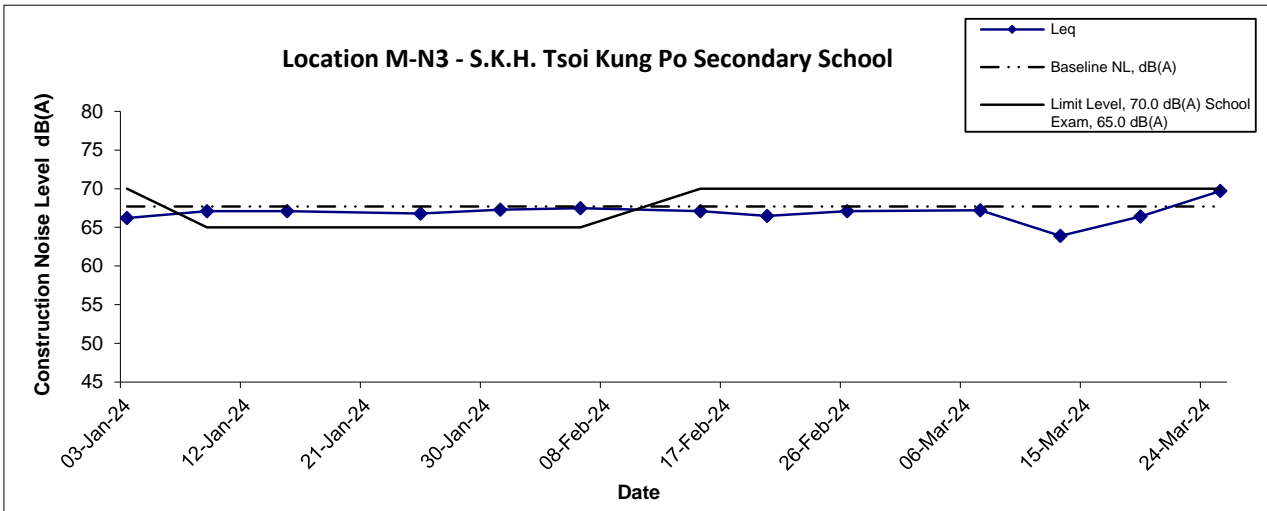

| | | | |
|--|----------------|------------------------|--|
| Title Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Graphical Presentation of Construction Noise Monitoring Results | Scale N.T.S | Project No. MA20024 | |
| | Date Mar-24 | Appendix G | |
