


Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)
Limit Level - 70.0 dB(A) / School Exam - 65.0 dB(A)

Location M-N3 - S.K.H. Tsoi Kung Po Secondary School							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
04-Mar-25	15:08	Sunny	66.4	69.8	57.2	67.7	66.4 Measured $\leq$ Baseline
10-Mar-25	14:00	Sunny	67.2	70.3	62.6	67.7	67.2 Measured $\leq$ Baseline
21-Mar-25	15:32	Sunny	68.4	70.4	64.9	67.7	60.1
27-Mar-25	16:15	Sunny	71.2	75.0	63.1	67.7	68.6

Noise Levels

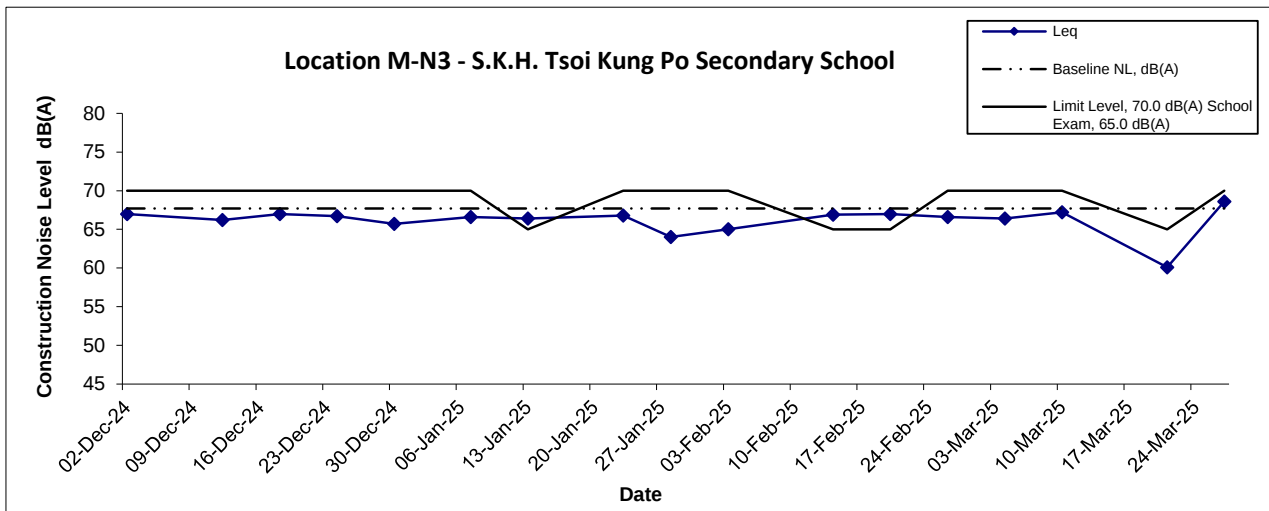

Title Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA20024	CINOTECH
	Date Mar-25	Appendix G	
