


Appendix F - 24-hour TSP Monitoring Results

Location M-A3 - S.K.H. Tsoi Kung Po Secondary School

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (hrs.)	Flow Rate (m³/min.)		Av. Flow (m³/min)	Total vol. (m³)	Conc. (µg/m³)	Action Level (µg/m3)	Limit Level (µg/m4)
				Initial	Final		Initial	Final		Initial	Final					
2-May-25	Sunny	300.1	759.0	2.8284	2.9009	0.0725	13339.5	13363.5	24.0	1.21	1.21	1.21	1735.9	41.8	153.0	<u>260.0</u>
6-May-25	Sunny	300.6	757.0	2.8250	2.9694	0.1444	13363.5	13387.5	24.0	1.20	1.20	1.20	1731.6	83.4		
12-May-25	Fine	298.9	759.7	2.8193	2.8835	0.0642	13387.5	13411.5	24.0	1.21	1.21	1.21	1741.0	36.9		
17-May-25	Rainy	301.9	758.9	2.8479	2.8967	0.0487	13411.5	13435.5	24.0	1.20	1.20	1.20	1729.9	28.2		
23-May-25	Fine	301.8	757.2	2.8269	2.8531	0.0262	13435.5	13459.5	24.0	1.20	1.20	1.20	1728.0	15.2		
28-May-25	Sunny	299.1	758.1	2.8211	2.8473	0.0262	13459.5	13483.5	24.0	1.21	1.21	1.21	1738.1	15.1		
													Min	15.1		
													Max	83.4		
													Average	36.7		

24-hr TSP Concentration Levels

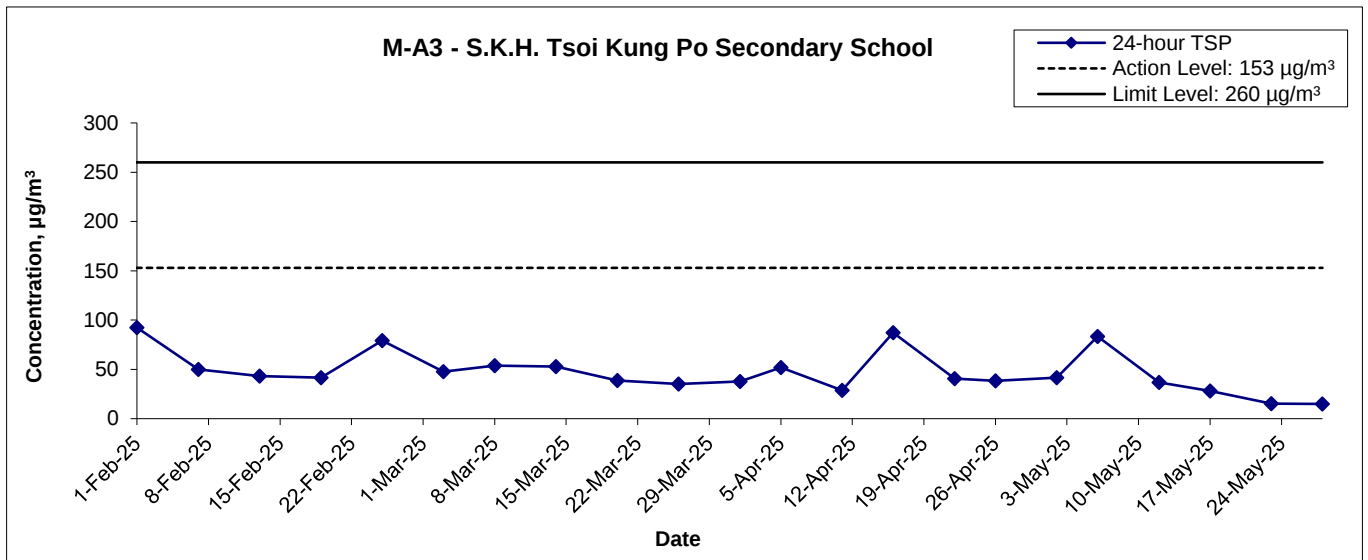

Title	Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Graphical Presentation of 24-hour TSP Monitoring Results	Scale	Project	CINOTECH
		N.T.S	No. MA20024	
		Date	Appendix	
		May 25	F	
