


Appendix F - 24-hour TSP Monitoring Results

Location M-A3 - S.K.H. Tsoi Kung Po Secondary School

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (hrs.)	Flow Rate (m³/min.)		Av. Flow (m³/min)	Total vol. (m³)	Conc. (µg/m³)	Action Level (µg/m3)	Limit Level (µg/m4)
				Initial	Final		Initial	Final		Initial	Final					
1-Nov-25	Cloudy	297.9	764.0	2.8217	2.8289	0.0072	14179.2	14203.2	24.0	1.23	1.23	1.23	1768.9	4.1	153.0	<u>260.0</u>
6-Nov-25	Fine	297.7	761.7	2.8789	2.8878	0.0089	14203.2	14227.2	24.0	1.23	1.23	1.23	1766.9	5.0		
12-Nov-25	Fine	294.8	761.1	2.8157	2.8508	0.0351	14227.2	14251.2	24.0	1.23	1.23	1.23	1774.4	19.8		
18-Nov-25	Fine	290.9	768.7	2.7960	2.8021	0.0061	14251.3	14275.3	24.0	1.24	1.25	1.25	1794.0	3.4		
24-Nov-25	Cloudy	295.7	765.0	2.8652	2.8733	0.0081	14275.3	14299.3	24.0	1.23	1.24	1.23	1776.2	4.5		
29-Nov-25	Fine	294.4	762.7	2.7893	2.8317	0.0424	14299.3	14323.3	24.0	1.24	1.23	1.23	1777.2	23.9		
													Min	3.4		
													Max	23.9		
													Average	10.1		

24-hr TSP Concentration Levels

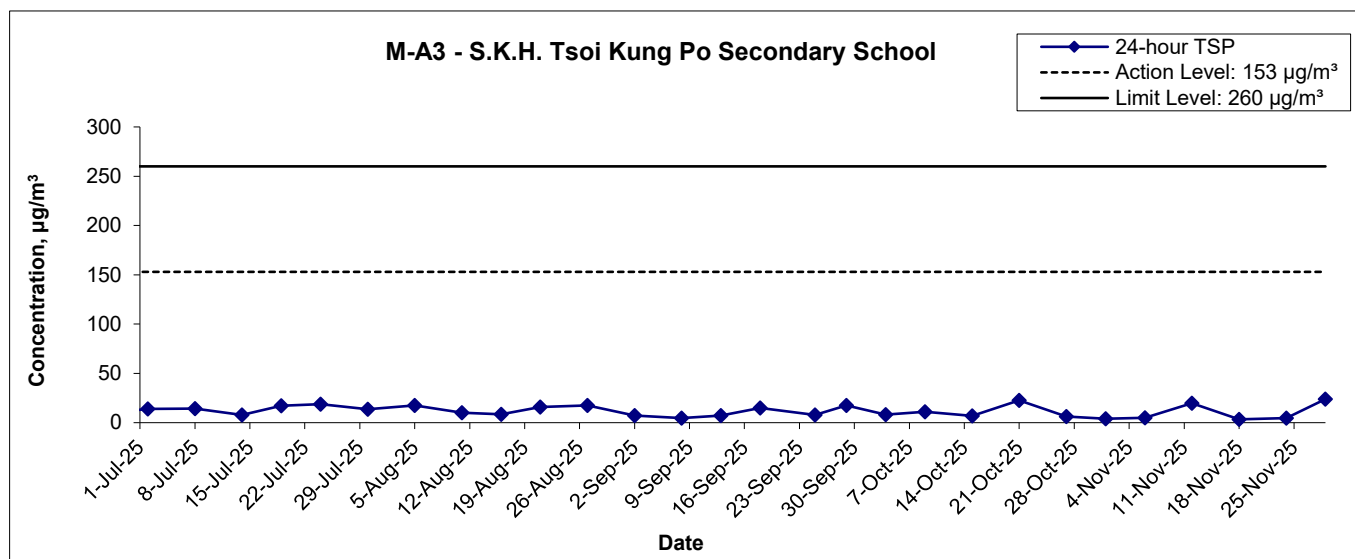

Remark:(1) Due the Super Tropical Cyclone signal Number 10 was hoisted on 24/09/2025 the Air Quality Monitoring on that day was cancelled.

Title	Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works	Scale	Project	CINOTECH
		N.T.S	No. MA20024	
Graphical Presentation of 24-hour TSP Monitoring Results		Date	Appendix	
		Nov 25	F	
